Hodge Construction Co.

Geneso CUSD #228
S.W. Elementary
Addition / Re-model
Geneseo, IL
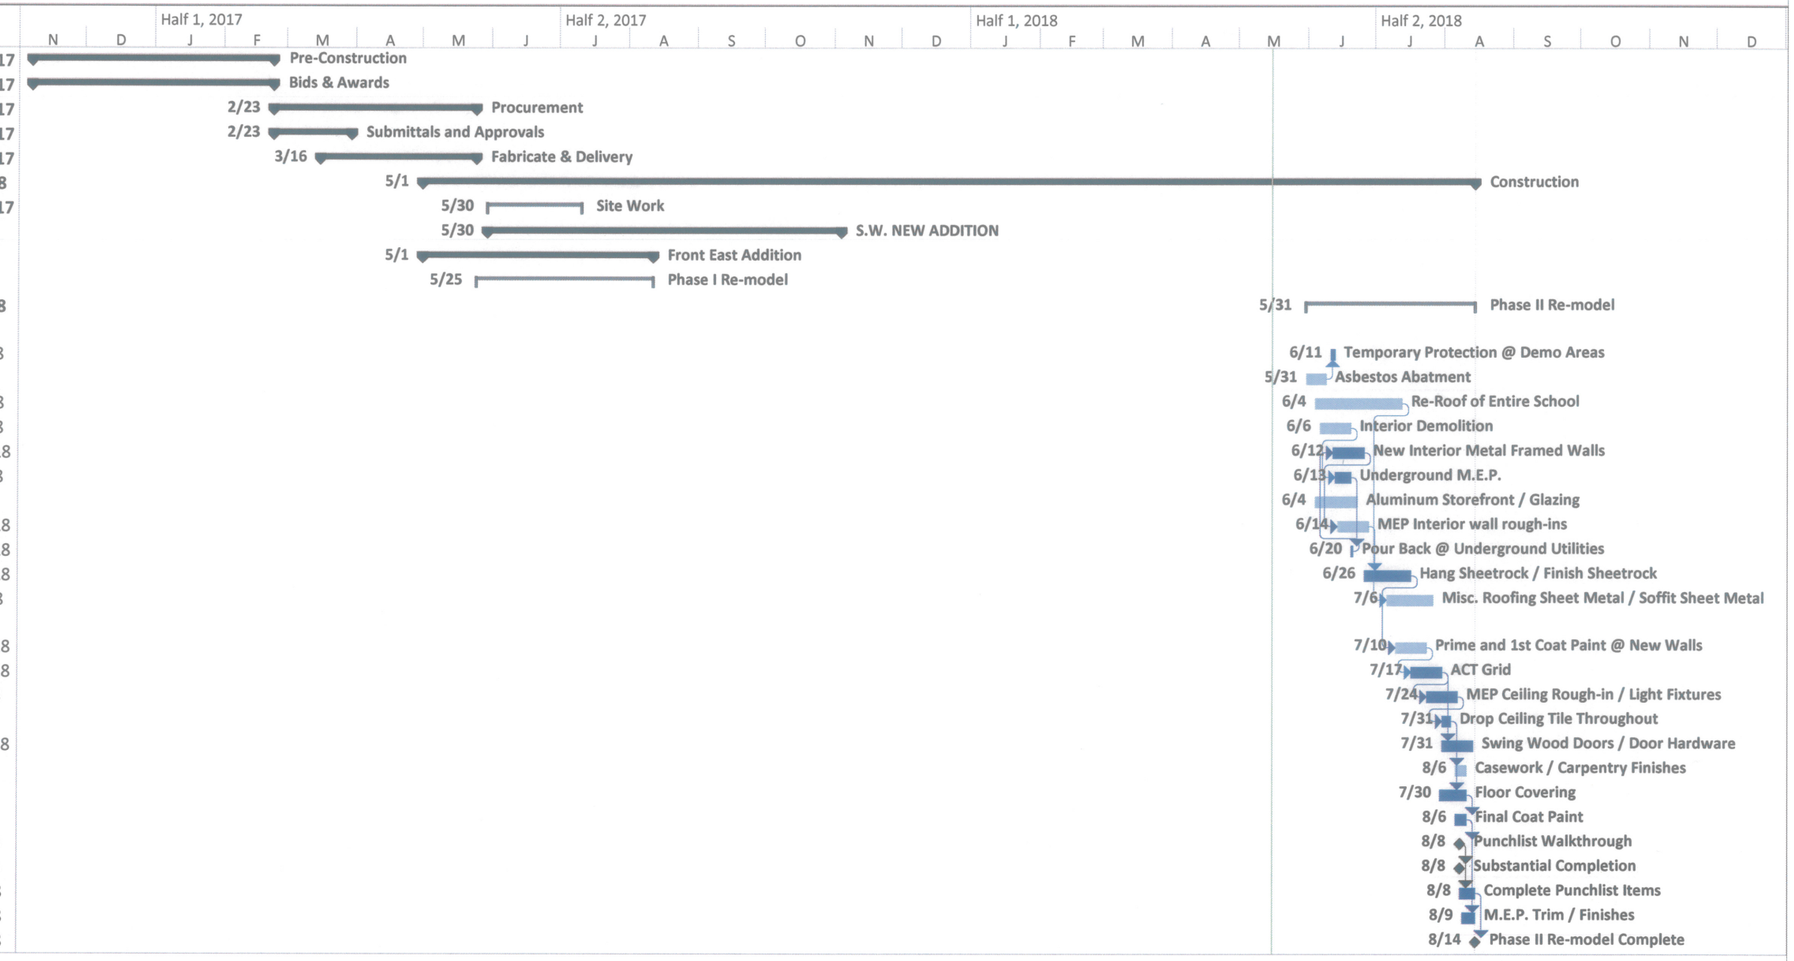
ID	Task Name	Duration	Start	Finish
1	**Pre-Construction**	**78 days**	**Mon 11/7/16**	**Wed 2/22/17**
2	**Bids & Awards**	**78 days**	**Mon 11/7/16**	**Wed 2/22/17**
9	**Procurement**	**65 days**	**Thu 2/23/17**	**Wed 5/24/17**
10	**Submittals and Approvals**	**25 days**	**Thu 2/23/17**	**Wed 3/29/17**
24	**Fabricate & Delivery**	**50 days**	**Thu 3/16/17**	**Wed 5/24/17**
38	**Construction**	**337 days**	**Mon 5/1/17**	**Tue 8/14/18**
39	**Site Work**	**30 days**	**Tue 5/30/17**	**Mon 7/10/17**
41	**S.W. NEW ADDITION**	**114 days**	**Tue 5/30/17**	**Fri 11/3/17**
69	**Front East Addition**	**75 days**	**Mon 5/1/17**	**Fri 8/11/17**
93	**Phase I Re-model**	**57 days**	**Thu 5/25/17**	**Fri 8/11/17**
116	**Phase II Re-model**	**54 days**	**Thu 5/31/18**	**Tue 8/14/18**
117	Temporary Protection @ Demo	2 days	Mon 6/11/18	Tue 6/12/18
118	Asbestos Abatment	7 days	Thu 5/31/18	Fri 6/8/18
119	Re-Roof of Entire School	29 days	Mon 6/4/18	Thu 7/12/18
120	Interior Demolition	10 days	Wed 6/6/18	Tue 6/19/18
121	New Interior Metal Framed Wal	10 days	Tue 6/12/18	Mon 6/25/18
122	Underground M.E.P.	5 days	Wed 6/13/18	Tue 6/19/18
123	Aluminum Storefront / Glazing	15 days	Mon 6/4/18	Fri 6/22/18
124	MEP Interior wall rough-ins	10 days	Thu 6/14/18	Wed 6/27/18
125	Pour Back @ Underground Utili	1 day	Wed 6/20/18	Wed 6/20/18
126	Hang Sheetrock / Finish Sheetrc	15 days	Tue 6/26/18	Mon 7/16/18
127	Misc. Roofing Sheet Metal / Soffit Sheet Metal	15 days	Fri 7/6/18	Thu 7/26/18
128	Prime and 1st Coat Paint @ Nev	10 days	Tue 7/10/18	Mon 7/23/18
129	ACT Grid	10 days	Tue 7/17/18	Mon 7/30/18
130	MEP Ceiling Rough-in / Light Fix	10 days	Tue 7/24/18	Mon 8/6/18
131	Drop Ceiling Tile Throughout	4 days	Tue 7/31/18	Fri 8/3/18
132	Swing Wood Doors / Door Hard	10 days	Tue 7/31/18	Mon 8/13/18
133	Casework / Carpentry Finishes	5 days	Mon 8/6/18	Fri 8/10/18
134	Floor Covering	10 days	Mon 7/30/18	Fri 8/10/18
135	Final Coat Paint	5 days	Mon 8/6/18	Fri 8/10/18
136	Punchlist Walkthrough	0 days	Wed 8/8/18	Wed 8/8/18
137	Substantial Completion	0 days	Wed 8/8/18	Wed 8/8/18
138	Complete Punchlist Items	5 days	Wed 8/8/18	Tue 8/14/18
139	M.E.P. Trim / Finishes	4 days	Thu 8/9/18	Tue 8/14/18
140	Phase II Re-model Complete	0 days	Tue 8/14/18	Tue 8/14/18
